



GOVERNMENT OF ODISHA

DEPARTMENT OF WATER RESOURCES

ANNUAL REPORT

OF

KANPUR CANAL DIVISION,
JHUMPURA(2015-16)

Executive Engineer,
Kanpur Canal Division,
Jhumpura

1. PROJECT IN BRIEF:--

Odisha state is very rich in water resources. Baitarani Basin is one of these resources. Kanpur Multipurpose Mega Irrigation Project on Upper Baitarani Basin after completion will provide irrigation to 29,578 Ha land in Keonjhar District (5 blocks, 36 Panchayats & 244 villages).

2. KANPUR CANAL DIVISION (JURISDICTIONS):-

- A. Kanpur Main Canal from RD 480m to RD 38610m
- B. Distribution system of KMC from RD 00m to RD 38610m
- C. Maintenance of Kanjhari Irrigation Project

A. KANUPUR MAIN CANAL:

- Kanpur Irrigation Project has only one Right Main Canal (78,21 Km) off taking at RD 2460M. of the Dam Axis.
- Kanpur Main Canal from RD 480m to RD 38610m is under the jurisdiction of this Division.
- The work of Main Canal under this Division has been completed 70%.
- The following works of KMC are under progress to complete the Main Canal upto 38610m.

a) Construction of Kanpur Main Canal from RD 21,600M to 38610M including structures, except the reach from RD 31950M to 32190 M of Kanpur Irrigation Project.

i.	Agency: -	M/s D.D. Builders Ltd.
ii.	Agreement no-	27F ₂ /2013-14
iii.	Date of commencement-	03.03.2014
iv.	Stipulated date of completion:-	02.03.2016.
v.	EOT Sanctioned -	02.09.2017.
vi.	Agreement value -	Rs.46,96.41 Lakh.
vii.	Work done-	Rs 2077.42 Lakh (44.23 %)




KMC at RD 30300m inspected by CE and MIS officials.



Boulder Grouted with Sand is in progress in Foundation of CD-47 at RD 38400m of KMC



Pile Load Test at CD-40 is in progress

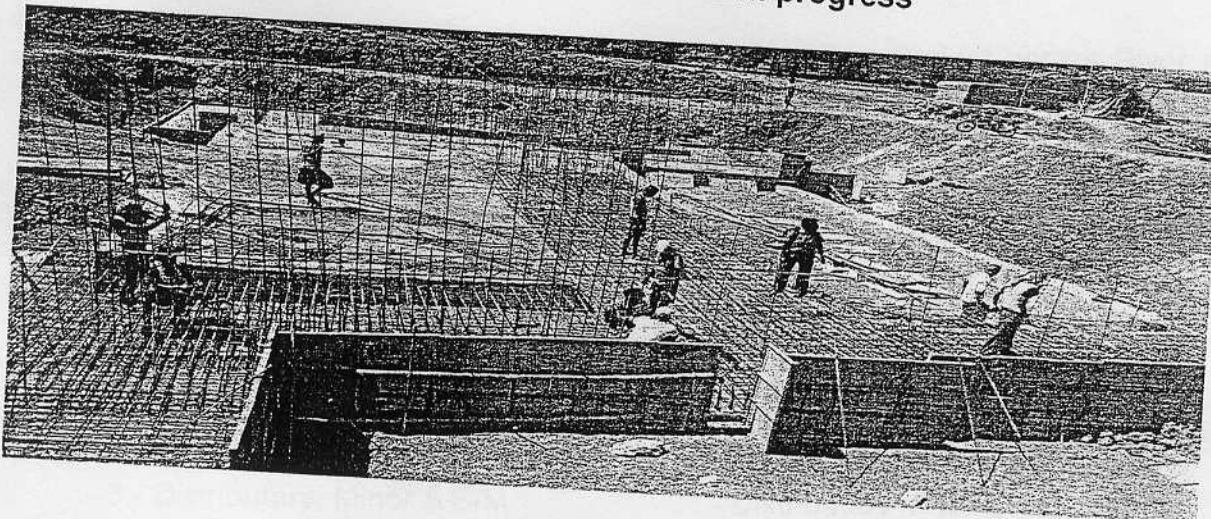

CR at RD 37630m of KMC in Progress.

