

GOVERNMENT OF ODISHA



DEPARTMENT OF WATER RESOURCES

KANUPUR IRRIGATION PROJECT, KEONJHAR

**ANNUAL REPORT
OF
KANUPUR CANAL DIVISION NO.II,
REMULI**

Executive Engineer,
Kanupur Canal Division No.II,
Remuli

Jurisdiction of the Division:-

Kanupur Canal Division No.II,Remuli was created vide DOWR Lr. No. 5417,

Dt. 27.02.2012 and became functional on dt.21.01.2014.

The jurisdiction of this division has been fixed vide CE,K.I.P,Keonjhar Lr. No.5591,dt.31.10.2014

As follows:-

- i) Construction of Kanupur Main Canal from RD 38610m to 78210m.
- ii) Distribution system of KMC Off-taking from RD 38610m to 78210m.

Further, the following works are entrusted upon this division subsequently as:-

- iii) Maintenance of Kanupur Irrigation Colony, Keonjhar.
- iv) Maintenance of Kanupur Irrigation Colony, Remuli.
- v) Maintenance of Rest Shed of Kanupur irrigation Project, Keonjhar.
- vi) Maintenance of CE Office,KIP, Keonjhar, SE Office,Jhumpura and FA&CAO Office, Keonjhar.

Under this division, three sub divisions function as follows:-

- 1) Kanupur Canal Sub division No.IV,Remuli
- 2) Kanupur Canal Sub division No.V,Remuli
- 3) Kanupur Canal Sub division No.VI,Jhumpura

Jurisdiction of Sub divisions:-

Name of the Sub division	Name of Canal with R.D	Name of Distribution System with R.D
Kanupur Canal Sub division No.IV,Remuli	Kanupur Main Canal from RD 39450M to 50790M	Distributries, Minors & Sub-minors of Kanupur Main Canal off-taking from RD 67700M to 78210M
Kanupur Canal Sub division No.IV,Remuli	Kanupur Main Canal from RD 50790M to 67470M	Distributries, Minors & Sub-minors of Kanupur Main Canal off-taking from RD 61280M to 67700M
Kanupur Canal Sub division No.VI,Jhumpura	Kanupur Main Canal from RD 38610M to 39450M including Aqueduct & RD 67470M to 78210M(Tail)	Distributries, Minors & Sub-minors of Kanupur Main Canal off-taking from RD 39154M to 61200M

EXECUTIVE ENGINEER

STAFF STRENGTH :-

Sl.No.	Name of the Post	Sanction strength	Men in position	Remarks
1	Executive Engineer	1	1	
2	Asst.Executive Engineer	3	2	One no.vacancy
3	Junior Engineer(Estimator)	1	1	
4	Asst. Engineer	4	4	
5	Junior Engineer	2	2	

SALIENT FEATURES OF KANUPUR CANAL SYSTEM UNDER THIS DIVISION:-

Total ayacut under this division = 22,089.00Ha.

No. & Name of Blocks covered up = 04

(Jhumpura, Champua, Keonjhar Sadar and Patna)

Sl. No.	Type of Canal	No. of Canal	Length	No. of Village covered	Remarks
1.	K.M.C	01	39.60KM	28	
2.	Distributaries	05	51.80KM	127	
3.	Minors	30	101.03KM		
4.	Sub-minors	59	74.455KM		

EXECUTIVE ENGINEER

5. STRUCTURE DETAILS OF CANAL SYSTEM:-


NAME OF THE CANAL	CD/AQUEDUCT	VRB/PMGSYB/ODRB	H/R	C/R / C/R CUM ESCAPE	FALL	DIRECT OUTLET
Kanupur Main Canal with RD 38450M to 78210M	31	24	25	04	NIL	17
Distribution System including Minors & Sub minors from RD 41190M to 78210M	49	206	73	Nil	975	859
TOTAL =	80	230	98	04	975	876

EXECUTIVE ENGINEER

STATUS OF STRUCTURES OF KANUPUR MAIN CANAL FROM RD 38610M TO 78210M

Sl. No.	Name of Structures	No.s	Drawing received	Balance	Data Submitted to CE(D)	Compliance to be made	Data to be submitted	Remarks
1	C.D	30	11	19	5	1	14	
2	C.R	2	1	1	0	0	1	
3	C.R cum Escape	2	0	2	0	0	2	
4	Direct Outlet	17	0	17	0	0	17	
5	H.R	25	6	19	0	0	19	
6	V.R.B	12	1	11	3	0	8	
7	P.M.G.S.Y Road Bridge	5	2	3		1	2	
8	ODR Bridge	3	0	3	1	0	2	
9	MDR Bridge	1	0	1	1	0	0	Data submitted to EE, R&B Division,Knjr
10	NH Crossing Bridge	1	0	1	1	0	0	Data submitted to EE,N.H Division,Knjr
11	Aqueduct	1	1	0	0	0	0	

SCHEMATIC DIAGRAM OF DISTRIBUTION NETWORK OF KANUPUR CANAL DIVISION NO.II,REMULI, KEONJHAR.

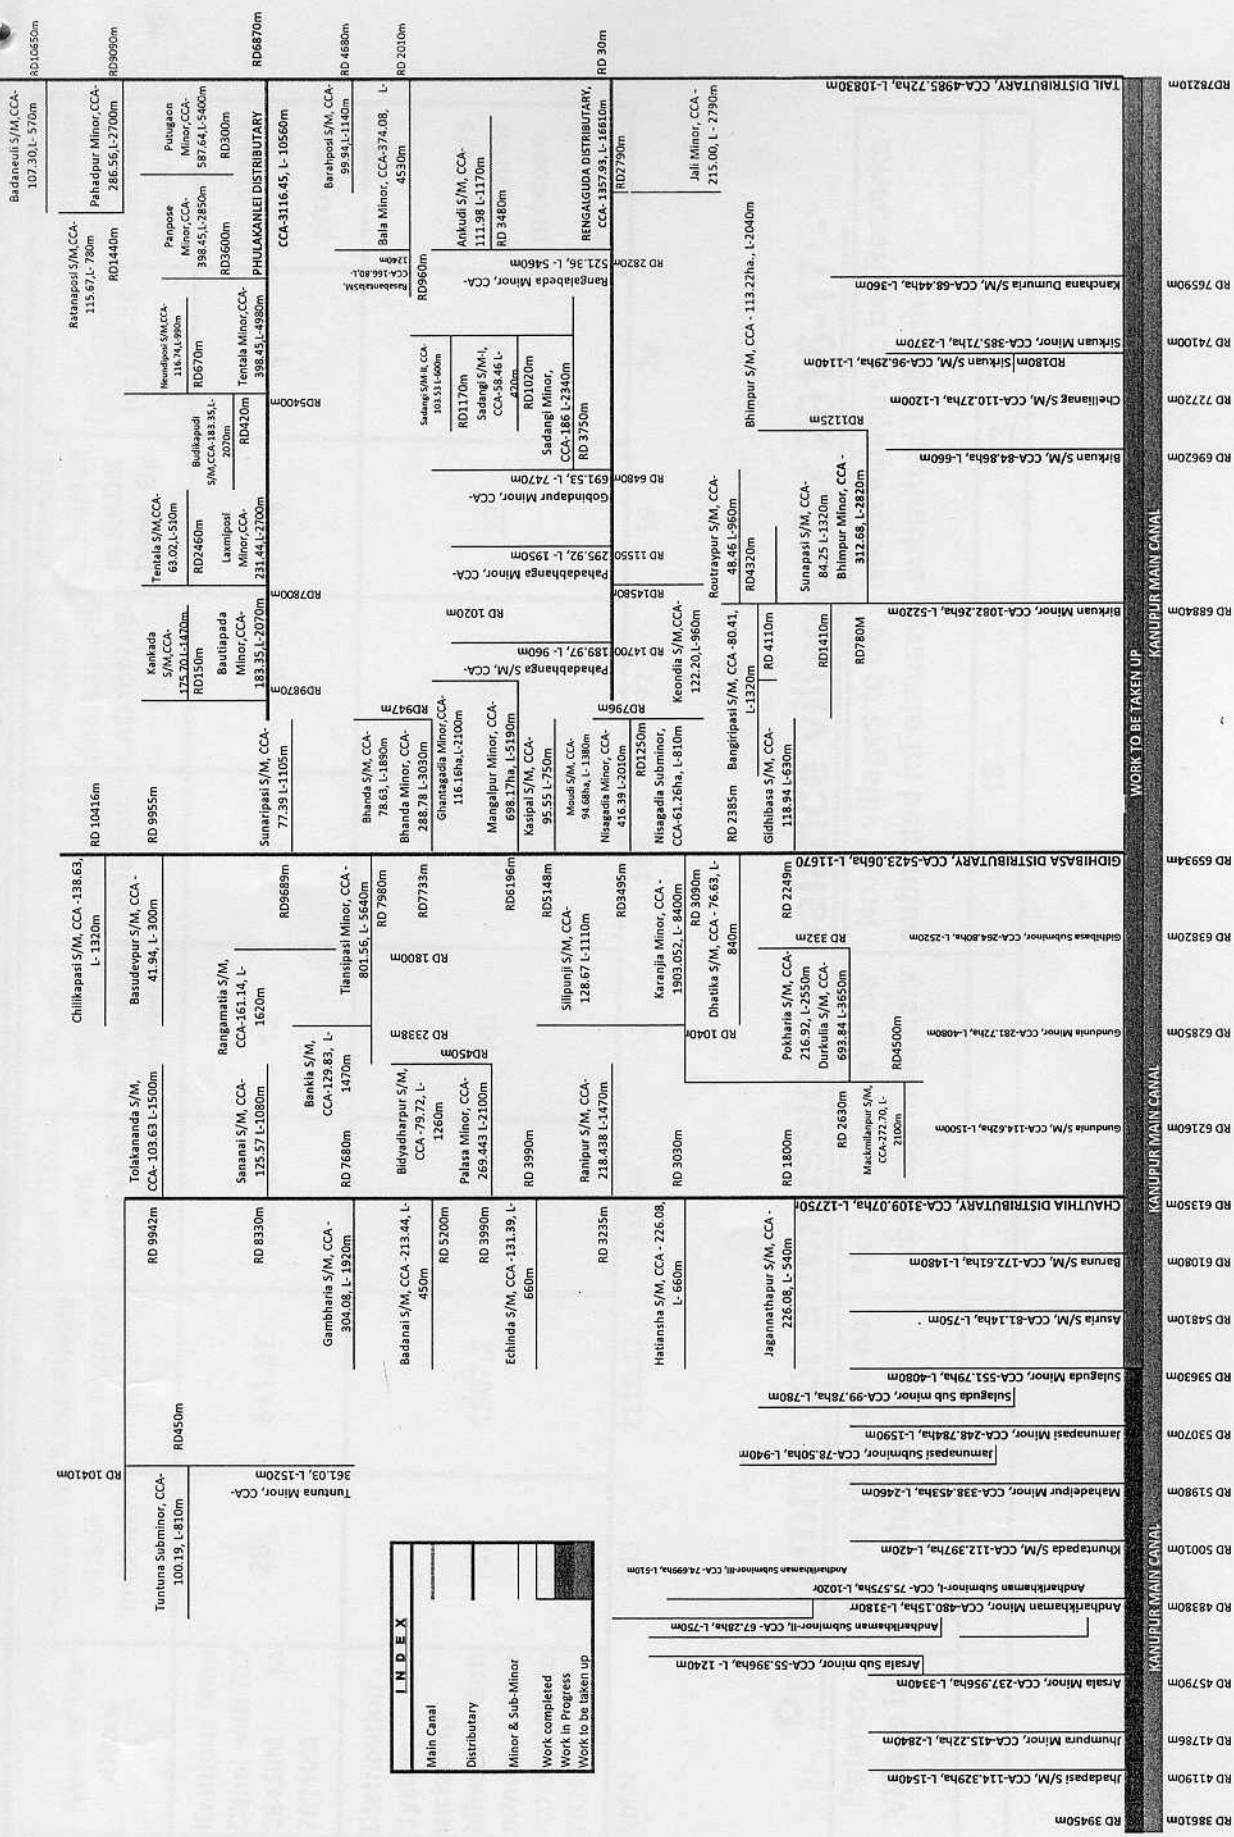

INDEX	
Main Canal	
Distributary	
Minor & Sub-Minor	
Work completed	
Work in Progress	
Work to be taken up	

WORK TO BE TAKEN UP

KANUPUR MAIN CANAL

KANUPUR MAIN CANAL

KANUPUR MAIN CANAL

